




MASON STREET BRIDGE

REPLACEMENT



PROJECT

LOCATION

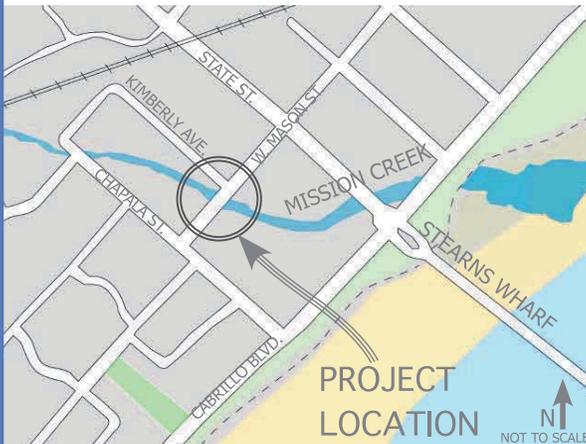

MASON STREET BRIDGE OVER MISSION CREEK
BETWEEN STATE ST. & CHAPALA ST.

PROJECT OVERVIEW

The Mason Street Bridge Replacement Project is one of three bridges being replaced over Mission Creek in the lower State Street vicinity. The bridge, built in 1946, has been deemed structurally deficient by CALTRANS and will be replaced to meet current structural standards. The new bridge design will:

- Increase flood capacity
- Increase habitat for the steelhead trout & tidewater gobies
- Improve safety
- Improve street lighting, sidewalks, landscape, & bridge railings

CONSTRUCTION SCHEDULE

WINTER 2016

FUNDING

FEDERAL HIGHWAY BRIDGE PROGRAM

COST

\$7 MILLION



RENDERING OF MASON ST. BRIDGE

MASON STREET BRIDGE REPLACEMENT PROJECT

Construction will include:

- Building demolition
- Bridge replacement
- New channel walls
- Expanded habitat zones
- Kimberly Ave. realignment

There will be area closures during the Mason Street Bridge improvements and detour signage to reduce neighborhood impacts as much as possible. Please see detour map at :

www.santabarbaraca.gov/CabrilloBridgeDetours



construction information

For more information,
Please call
Project Information Line
805.897.2637
City Website: www.SantaBarbaraCA.gov

* For monthly construction updates, please go to the City's website. You will find more information at the "Major Construction Projects" link.

MASON STREET BRIDGE REPLACEMENT PROJECT CONSTRUCTION SCHEDULE

ID	Task Name	Start	Finish	Qtr 3, 20	Qtr 4, 20	Qtr 1, 20	Qtr 2, 20	Qtr 3, 20	Qtr 4, 20	Qtr 1, 20	Qtr 2, 20	Qtr 3, 20	Qtr 4, 20	Qtr 1, 20	Qtr 2, 20
1	Mason Street Bridge Replacement Project	Mon 10/13/14	Tue 12/13/16												
2	Notice to Proceed	Tue 10/14/14	Tue 10/14/14												
3	East Creek Wall Construction	Tue 10/14/14	Fri 6/19/15												
4	Demo Building 15 & 16 West Mason	Mon 10/27/14	Wed 11/5/14												
5	Remove Contaminated Soil, Others	Thu 11/6/14	Thu 11/13/14												
6	Utilities Relocation	Mon 10/20/14	Tue 6/16/15												
7	West Creek Wall Construction	Wed 6/24/15	Mon 3/21/16												
8	Bridge	Mon 4/18/16	Tue 12/13/16												
9	Landscaping	Mon 5/23/16	Wed 11/30/16												
10	Plant Establishment Period	Wed 11/30/16	Wed 5/31/17												
11	New Utilities & Roadwork	Tue 10/4/16	Thu 11/17/16												
12	Ornamental Fence	Fri 10/28/16	Wed 11/9/16												
13	Utility Relocation - Cox, Verizon, SCE	Tue 11/15/16	Thu 12/15/16												
14	Remove Street Closure	Tue 12/13/16	Tue 12/13/16												

Project: 11-1-2016 City Project Schedu
Date: Fri 11/4/16

Task



Milestone ◆

Progress

